

Project update

Congleton town centre improvements

Dear sir / madam,

Plans to change Congleton town centre have been finalised following extensive consultation with the local community. The scheme has started, and will deliver junction improvements and an enhanced town centre environment over the coming months.

Progress report

Completed the laying of the granite blocks on the Duke Street carriageway.

Re-siting of existing construction barriers to open up Duke Street and adjacent footways.

Completed the laying of the granite blocks adjacent to the new granite bench.

Commence kerbing and footway works outside of the Natwest Bank on Market Street.

Photo Number 1 shows new granite paving adjacent to the proposed granite bench.

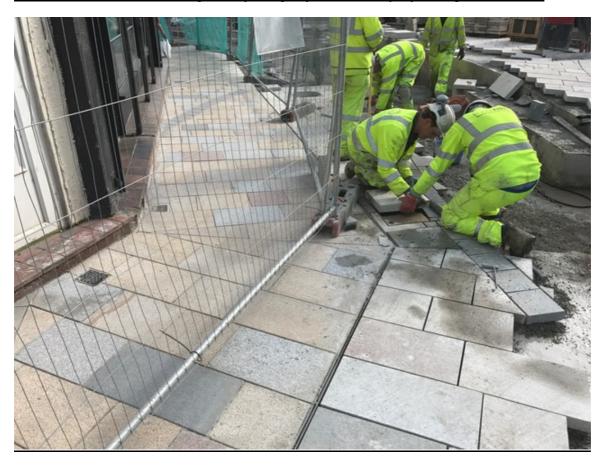


Photo Number 2 shows the new granite paving at the north east footway adjacent to Duke Street.


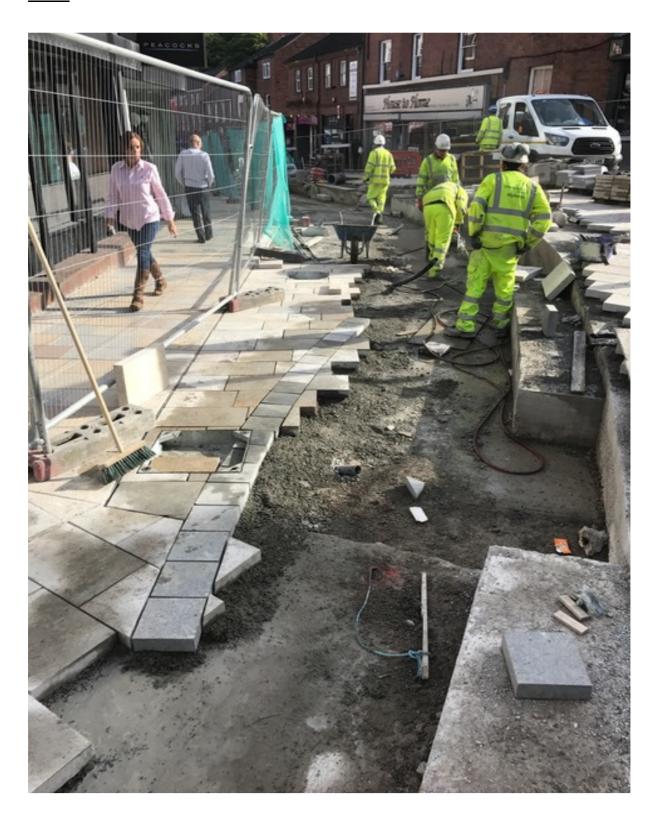


Photo number 3 shows the newly laid section of the north east footway paving at Duke Street up to the proposed granite bench.



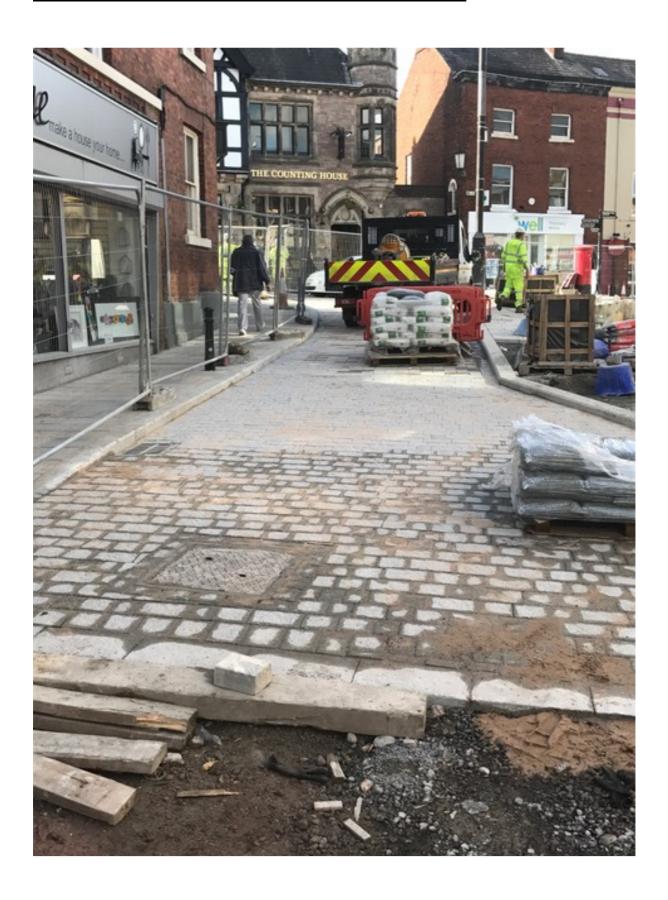

All works are currently on programme.

Looking ahead

Excavation of the footway at the south east corner of Market Street (outside the Natwest Bank). Lowering of the BT boxes outside of the Natwest Bank. Concreting the footway at the south east corner of Market Street. Installation of the granite paving at the south east corner of Market Street.

A road closure at Market Street will be in operation this coming Sunday – 08 October, to enable works to be carried out at this junction, safely.

All roadworks, closures and diversions are displayed on our roadworks map at www.cheshireeast.gov.uk/highways and roads/roadworks.

Keeping you informed

Detailed information about the scheme can be found online at www.cheshireeast.gov.uk/highways and live updates from site will be tweeted from @CECHighways, so please give us a follow.

Thank you for your patience whilst these improvements to Congleton town centre are delivered.

Yours faithfully,

Jon Berry Project Manager Cheshire East Highways
